

Date: Thursday, 10/07/2008 1:38:31 PM
User: Julie Lecocq

Process Sheet

Customer : CU-DAR001 Dart Helicopters Services	Drawing Name : X-TUBE AS 350/355 HI AFT UNDER REVIEW
Job Number : 40415	
Estimate Number : 13225	
P.O. Number :	Part Number : D350748241TRN
This Issue : 10/07/2008 S.O. No. :	Drawing Number : D350-748-241 REV.D
Prsht Rev. : NC	Project Number : N/A
First Issue : / / Type : CROSSTUBES	Drawing Revision : D
Previous Run : 40414	Material :
Written By :	Due Date : 17/07/2008 Qty: 1 Um: Each
Checked & Approved By : <u>JUL 08.7.10</u>	
Comment : Est Rev:A New Issue 08-03-06 DD verified by:ec Est Rev B Removed polish 08.04.02 EC verified by : DD Est Rev C Removed LPS-3 08.06.23 Ec verified by: DD	

Additional Product

Job Number:



Seq. #:	Machine Or Operation:	Description :
---------	-----------------------	---------------

1.0	D6018125	Crosstube Material
-----	----------	--------------------



Comment: Qty.: 1.0000 Each(s)/Unit Total : 1.0000 Each(s)
Crosstube Material
D6018-125
2.299" OD X 2.000" ID
Batch: 327472

am 08.07.25 ①

2.0	MORI SEIKI	MORI SEIKI CNC LATHE LARGE
-----	------------	----------------------------

**Comment:** MORI SEIKI CNC LATHE LARGE

1-Fill tube with sand & install plugs on both ends as per Folio FA647

2-Turn first side as per Folio FA647

3- File transition lines smooth.

am 08.07.15 ①

3.0	QC1	INSPECT ALL DIM TO DIM SHEET
-----	-----	------------------------------

**Comment:** INSPECT ALL DIM TO DIM SHEET

am 08.07.15 ②

4.0	MORI SEIKI	MORI SEIKI CNC LATHE LARGE
-----	------------	----------------------------

**Comment:** MORI SEIKI CNC LATHE LARGE

1-Turn second side as per Folio FA647

2- File transition lines smooth.

am 08.07.15 ③

Dart Aerospace Ltd

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Date: Thursday, 10/07/2008 1:38:31 PM
User: Julie Lecocq

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: X-TUBE AS 350/355 HI AFT UNDER REVIEW

Job Number: 40415

Part Number: D350748241TRN

Job Number:



Seq. #:

Machine Or Operation:

Description :

3-Scribe part # as per Dwg D350-748-241

Am 08-07-15 ①

5.0

QC1

INSPECT ALL DIM TO DIM SHEET



Comment: INSPECT ALL DIM TO DIM SHEET

Am 08-07-15 ①

6.0

QC8

SECOND CHECK



ANM 7-7-15



Comment: SECOND CHECK

7.0

OUTSIDE SERV.10

OUTSIDE SERVICES -skids



Comment: Sub-Contracting OUTSIDE SERVICES

Issue P/O: 7012

Heat Treat to min 180 KSI As per Dwg D350-748-241

Sand Blast tube after Heat Treat

Possible Supplier: Vac Aero

Ensure Certificate of Conformity is attached

C208108125

①

8.0

PACKAGING 1

PACKAGING RESOURCE #1



Comment: PACKAGING RESOURCE #1

Receive & Inspect For Transit Damage

Ensure certificate of conformity is attached

PC 8/9/25 ①

9.0

QC6

DIMENSIONAL CHECK



Comment: DIMENSIONAL CHECK

208108130 ①

10.0

PACKAGING 1

PACKAGING RESOURCE #1



Comment: PACKAGING RESOURCE #1

Identify and stock in kanban rack

Location: Back Hall

RT 08-09-30

11.0

QC21

FINAL INSPECTION/W/O RELEASE



Comment: FINAL INSPECTION/W/O RELEASE

08/09/30 ①

Job Completion



mf 08-09-30

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

DART AEROSPACE LTD		Work Order: 40415
Description: Crosstube Assembly (AS350/355 High Aft)		Part Number: D350-748-241
Inspection Dwg: D350-748-241 Rev: D		Page 1 of 1

FIRST ARTICLE INSPECTION CHECKLIST

☒

First Article

☐

Prototype

Inspection Sheet	Drawing Dimension	Tolerance	Actual Dimension	Accept	Reject	Method of Inspection	Comments
SIDE A	2.240	+0.005/-0.000	2.245	/			
	2.180	+0.005/-0.000	2.185	/			
	2.180	+0.005/-0.000	2.185	/			
	2.208	+0.005/-0.000	2.213	/			
	2.234	+0.005/-0.000	2.238	/			
	2.253	+0.005/-0.000	2.254	/			
	2.272	+0.005/-0.000	2.276	/			
	2.299	+0.005/-0.000	2.299	/			
	0.063	+/-0.010	0.063	/			
	4.26	+/-0.030	4.290	/			
	R0.063	+/-0.010	R0.063	/			
	R0.50	+/-0.030	R0.500	/			
SIDE B	2.240	+0.005/-0.000	2.245	/			
	2.180	+0.005/-0.000	2.185	/			
	2.180	+0.005/-0.000	2.185	/			
	2.208	+0.005/-0.000	2.213	/			
	2.234	+0.005/-0.000	2.238	/			
	2.253	+0.005/-0.000	2.254	/			
	2.272	+0.005/-0.000	2.276	/			
	2.299	+0.005/-0.000	2.299	/			
	0.063	+/-0.010	0.063	/			
	4.26	+/-0.030	4.290	/			
	R0.063	+/-0.010	R0.063	/			
	R0.50	+/-0.030	R0.500	/			
	122.70	+/-0.060					

Measured by: A. N	Audited by: A. M	Prototype Approval:	N/A
Date: 08-07-15	Date: 8-7-13	Date:	N/A
Rev	Date	Change	Revised by
A	07.01.17	New Issue (P/O D350-748-201)	KJ/JLM
			Approved

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

DART**RELEASED**

06-10-31

DESIGN 90	DRAWN BY 90	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
CHECKED H	APPROVED H	DRAWING NO. D350-748-241	REV. D SHEET 1 OF 3
DATE 06.10.31	TITLE CROSSTUBE (AS 350/355 HI AFT)		SCALE NTS
A	06.03.31	NEW ISSUE	
B	06.06.30	ADD D6018-125 & PRIME AND PAINT	
C	06.08.14	ADD CAD PLATING	
D	06.10.31	MAG. PARTICLE AND CAD PLATE AS MFD.	

QTY	P/N	DESCRIPTION
X	D350-748-241	CROSSTUBE ASSEMBLY (AS 350/355 HI AFT)
1	D6018-125	CROSSTUBE (OR D6015-125)
2	D3502-1	SUPPORT
2	D2856-400-710	ABRASION STRIP
1	AELS-1032-225	INSERT
1	AN960JD10	WASHER
2	MS21920-20	CLAMP (PER DART SPEC. M-MS21920-20)
1	MS27039-1-10	SCREW

D350-748-141 CROSSTUBE:

- 1) MATERIAL: MANUFACTURED FROM D6018-125 OR D6015-125
FINISHED LENGTH = 122.70 ± 0.06
- 2) MACHINE PER MACHINING DETAIL ON PAGE 3. BLEND OUT ALL EDGES FROM MACHINING LONGITUDINALLY, TRANSITIONS SHOULD BE SMOOTH. NOTE: ALL HOLES ARE DRILLED AFTER BENDING.
- 3) SCRIBE DART PART NUMBER AND BATCH NUMBER IN THIS AREA WITH VIBRATING STYLUS
- 4) BEND PROGRESSIVELY WITH A MINIMUM OF 7 PASSES. MAXIMUM TUBE FLATTENING DUE TO BENDING IS 6% BASED ON O.D.
- 5) HEAT TREAT TO MIN. 180 KSI PER MIL-T-6736 OR AMS 2759-1C AFTER TURNING
- 6) FINISH: MAGNETIC PARTICLE INSPECT PER DART QSI 038 4.2
CADMIUM PLATE PER AMS-QQ-P-416B, CLASS 1, TYPE II
PRIME INSIDE AND OUTSIDE PER DART QSI 005 4.2
PAINT OUTSIDE PER DART QSI 005 4.2
- 7) EXTREME CARE MUST BE TAKEN TO PROTECT THE OUTSIDE SURFACE OF THE TUBE. THE OUTSIDE SURFACE MUST BE SMOOTH AND FREE FROM SURFACE DEFECTS SUCH AS SCRATCHES, NICKS, OR DENTS. DEFECTS UP TO 0.005" MAY BE BLENDED OUT LONGITUDINALLY. CIRCUMFERENTIAL GRIND MARKS ARE UNACCEPTABLE. WHEN DRILLING HOLES EXTREME CARE MUST BE TAKEN AND CAREFUL DEBURRING PERFORMED TO ENSURE A CLEAN HOLE WITH NO CRACKING/CHIPPING/GROOVES.
- 8) INSTALL D2856-400-710 ABRASION STRIP WITH A GAP ON BOTTOM SIDE OF CROSSTUBE, CENTERED OPPOSITE D3502-1 SUPPORT, PER QSI 035.
- 9) TORQUE MS21920-20 CLAMPS 60 TO 80 IN-LB
- 10) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED.
- 11) ALL DIMENSIONS ARE IN INCHES
- 12) PART IS SYMMETRIC ABOUT CENTERLINE EXCEPT FOR $\varnothing 0.297$ HOLE.

UNDER REVIEW

07.02.16

OK 07.02.16

Copyright © 2006 by DART AEROSPACE LTD

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

Dart Aerospace Ltd




W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			


NOTE: Date & initial all entries

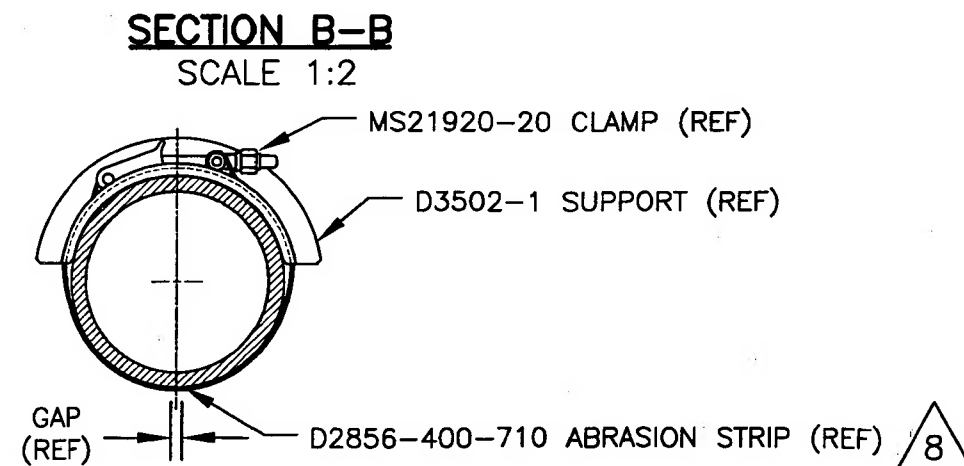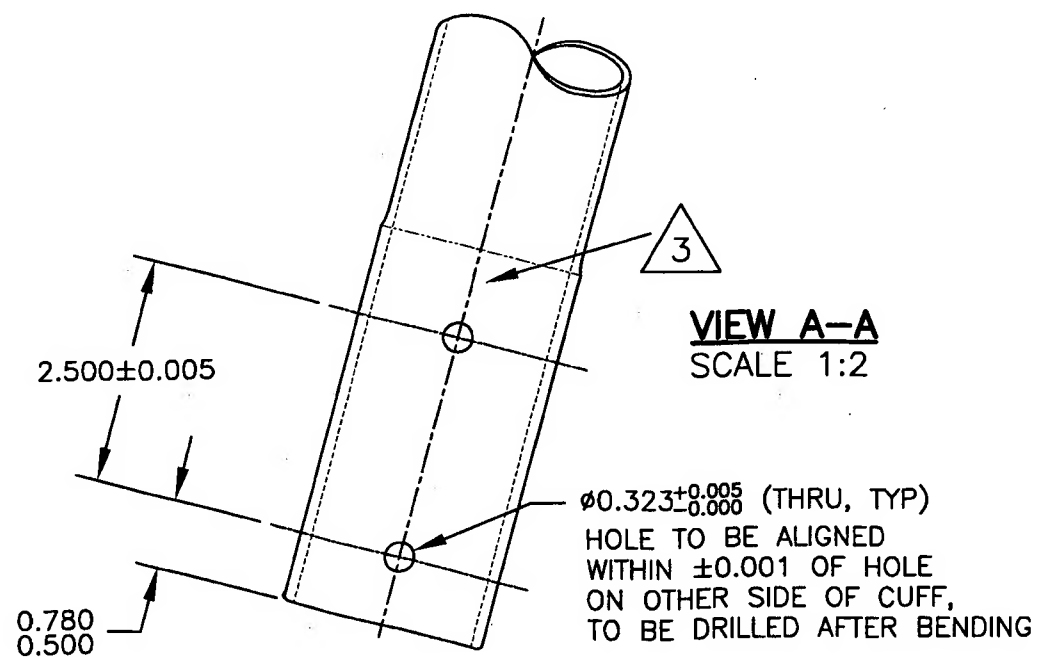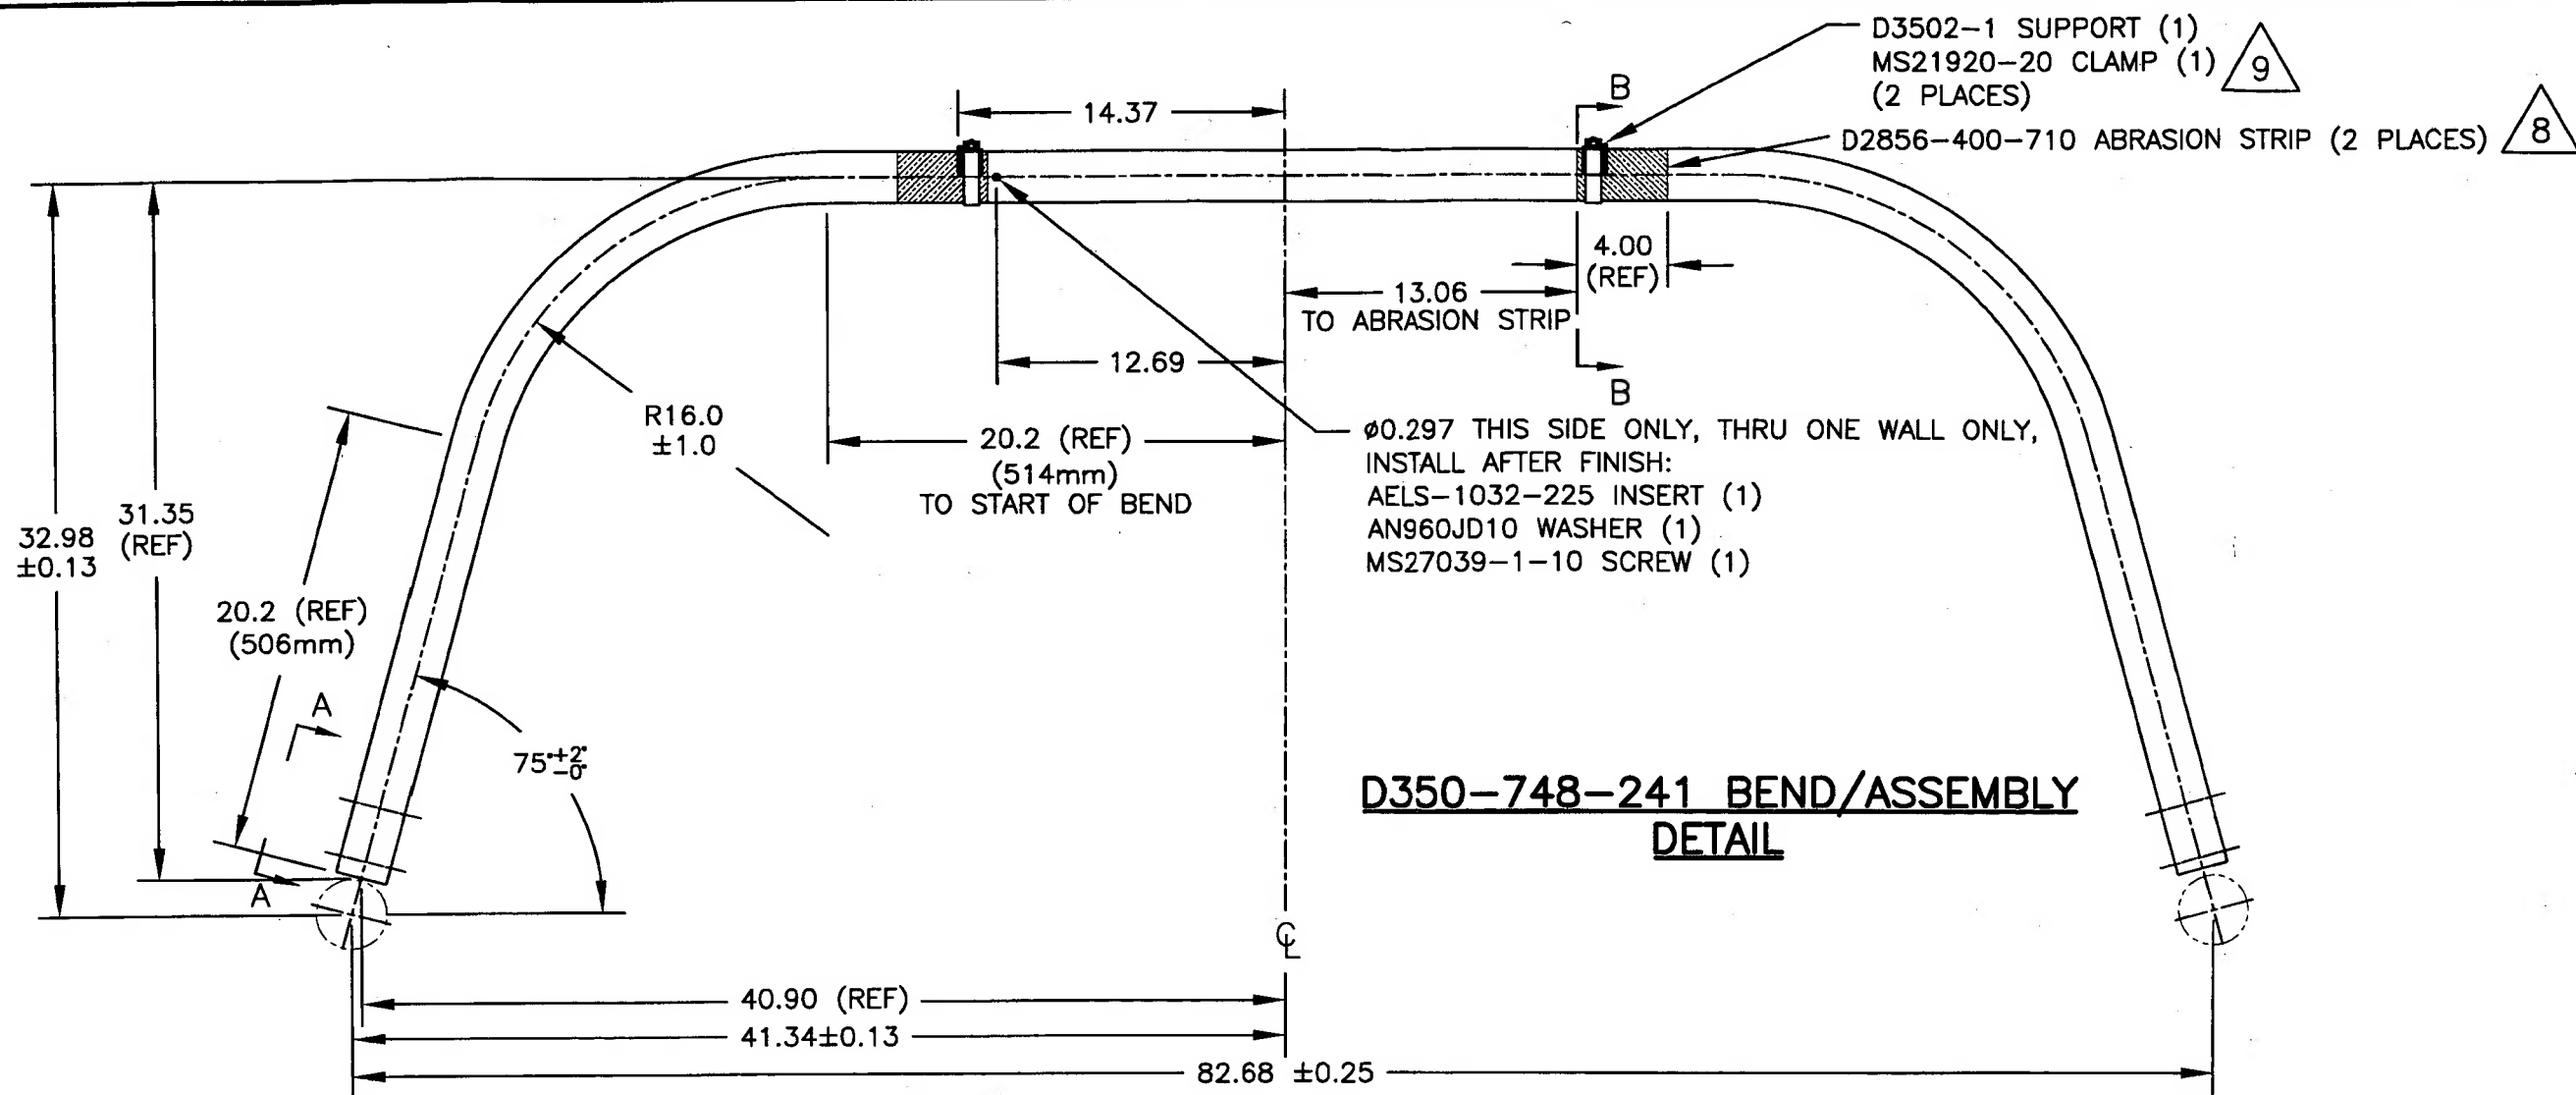

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 40415


UNDER REVIEW
07.02/16
CUFF REPAIR REDUCED
OK 07.10.22
RELEASED
06.10.31

COPYRIGHT © 2006 BY DART AEROSPACE LTD.		DESIGN	90	DRAWN BY	90	DART	DART AEROSPACE LTD. HAWKESBURY, ONTARIO, CANADA
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.		CHECKED	#	APPROVED	#	DRAWING NO.	REV. D
		DATE	06.10.31			D350-748-241	SHEET 2 OF 3
						TITLE	SCALE
						CROSSTUBE (AS 350/355 HI AFT)	1:8

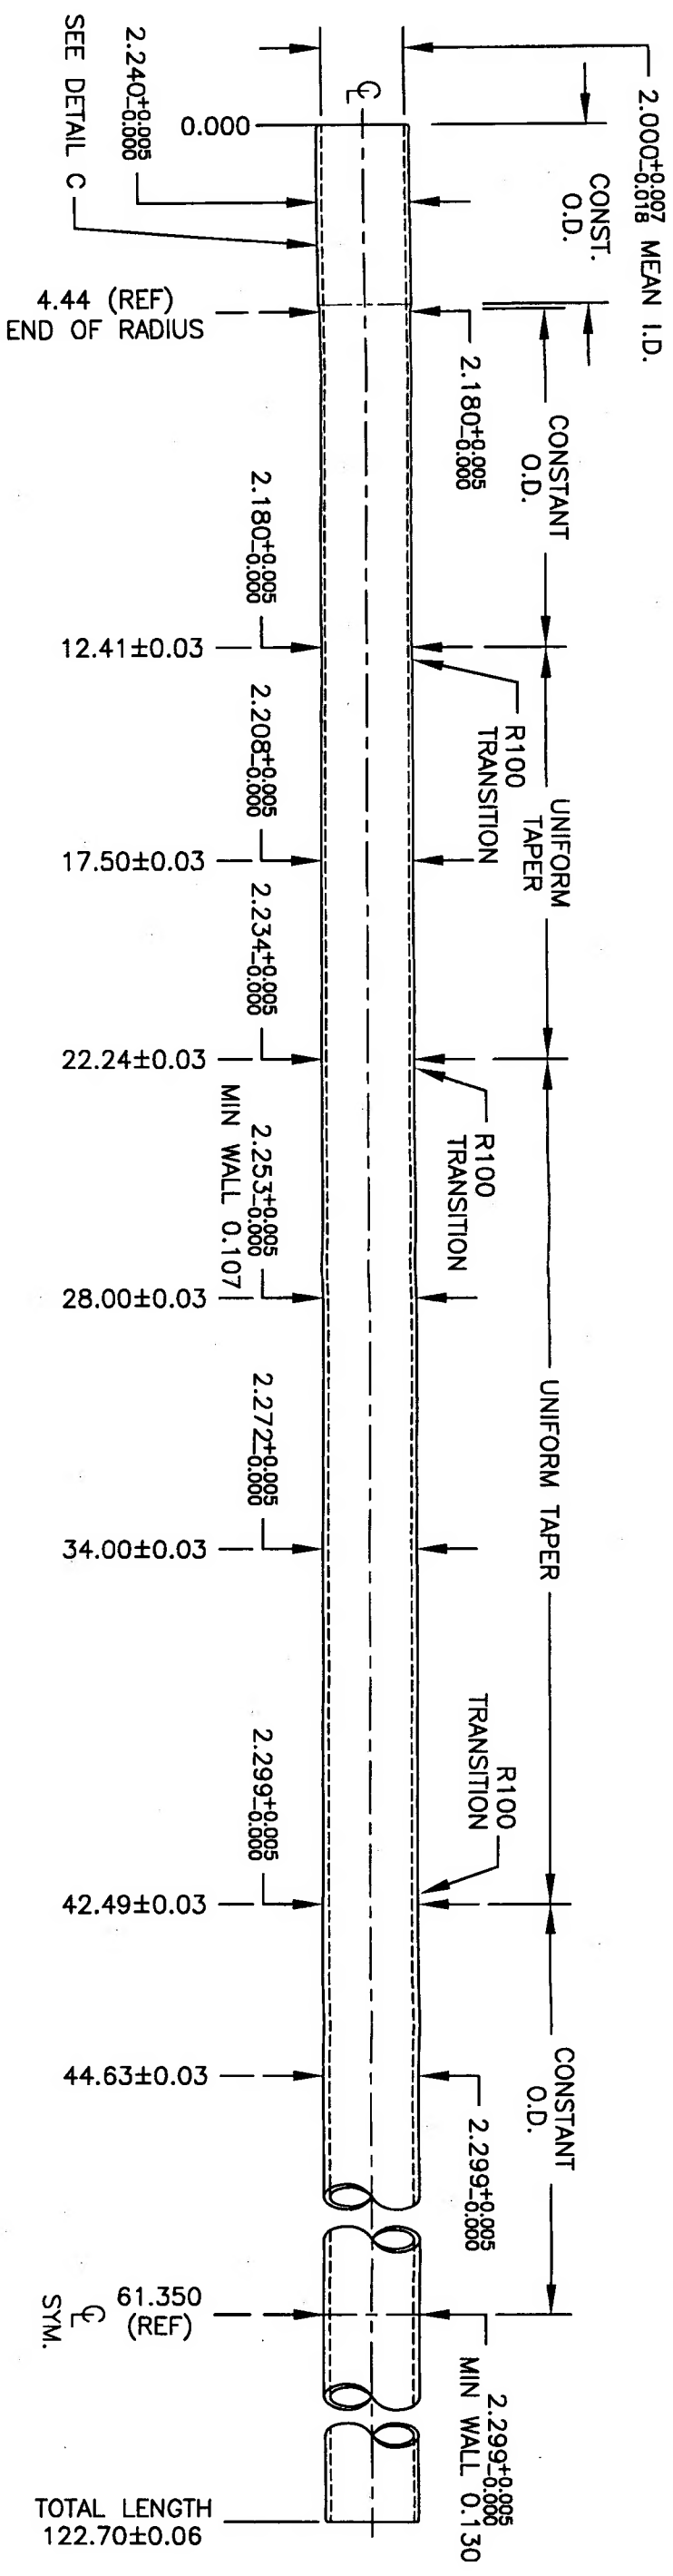


D350-748-241 MACHINING DETAIL

DETAIL C: CUFE
SCALE 1:1

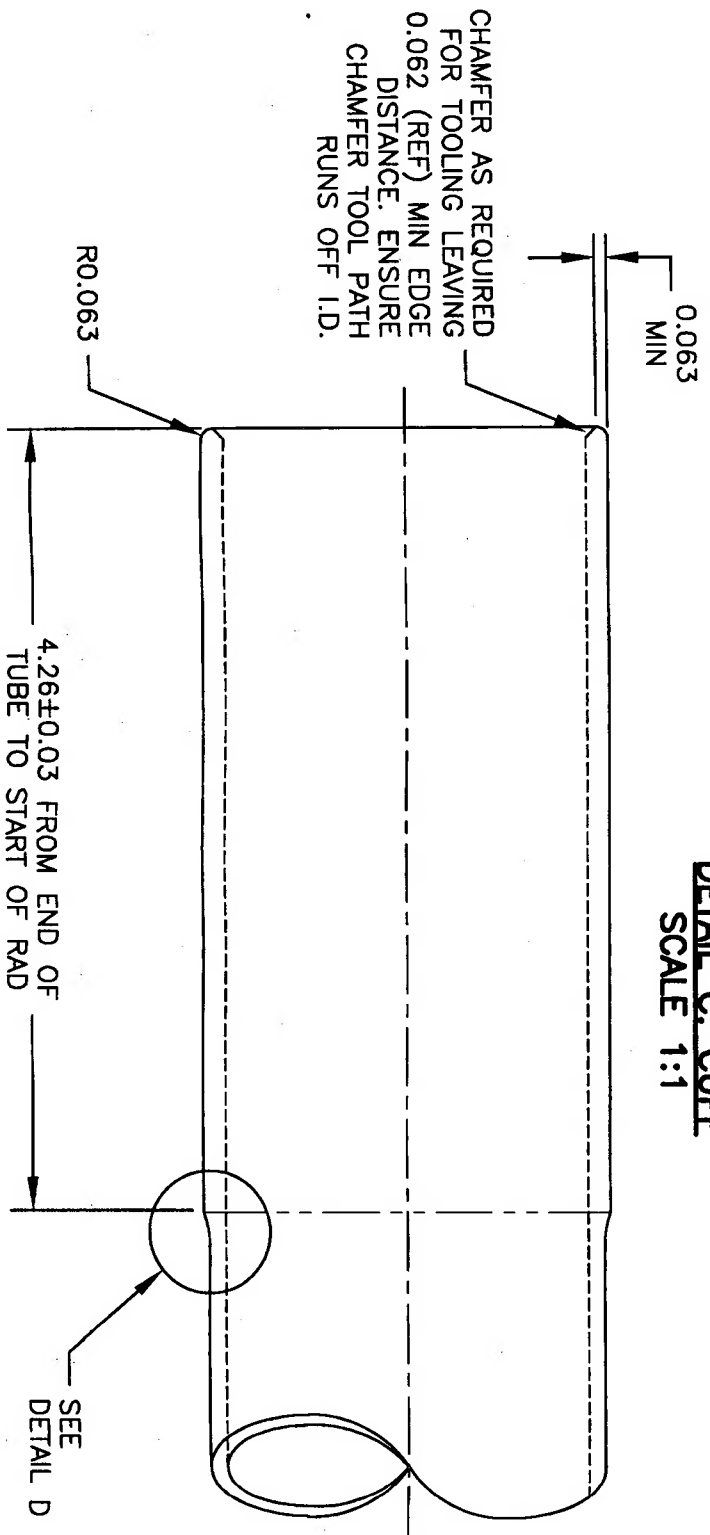

DETAIL D: CUFE TRANSITION
SCALE 9:1

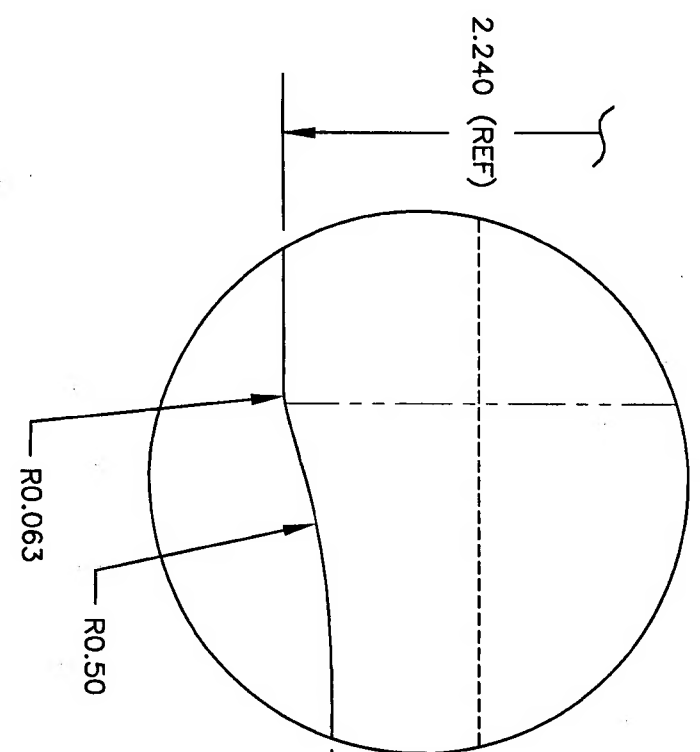


UNDER REVIEW
07.02/16
07.02/16
07.02/16

RELEASED
06.10.31

DESIGN <i>qp</i> DRAWN BY <i>qp</i> DART DART AEROSPACE LTD. <small>HAMMERSLEY, ONTARIO, CANADA</small>	
CHECKED <i>[Signature]</i> DATE 06.10.31	APPROVED <i>[Signature]</i> TITLE CROSSTUBE (AS 350/355 HI AFT)
DRAWING NO. D350-748-241 SHEET 3 OF 3 SCALE 1:4	REV. D

COPYRIGHT © 2006 BY DART AEROSPACE LTD.
 THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 40415



VAC AERO
INTERNATIONAL INC.

RELEASE NOTE

GST No.: R105468102

OAK 102442-1



HEAD OFFICE
1371 SPEERS ROAD, OAKVILLE, ONTARIO
CANADA L6L 2X5
TEL: (905) 827-4171 FAX: (905) 827-7489



2009 WYECROFT ROAD, UNIT B
OAKVILLE, ONTARIO
CANADA L6L 6J4
TEL: (905) 827-7377 FAX: (905) 827-1380



QUEBEC DIVISION
7450 RUE VÉRITÉ STREET, ST. LAURENT, QUÉBEC
CANADA H4S 1C5
TEL: (514) 334-4240 FAX: (514) 334-6269

09/26/2008

MM / DD / YYYY

PAGE: 1

BILL TO: 1DAR01
DART AEROSPACE LTD.
1270 ABERDEEN ST.
HAWKESBURY, ON

SHIP TO: DART AEROSPACE LTD.
1270 ABERDEEN ST.
HAWKESBURY, ON

K6A 1K7

K6A 1K7

DATE SHIPPED	SHIP VIA	F.O.B.
09/26/2008		ORIGIN
CUSTOMER P/O No.	JOB No.	TERMS
00007012		NET 30 DAYS

PART No.	DESCRIPTION	UOM	QTY ORD	QTY SHPD	TEST RESULTS
D350-748		EA	12	12	
<p>Process Specifications: Procedure: 4353 HEAT TREATED TO 180 KSI MIN. PER AMS 2759-1D 100% HARDNESS TESTED AS PER ASTM E-18, 40-45 HRC MATERIAL: 4130</p> <p>SAND BLASTED PARTS</p> <p>1 PIECE P/N D350-748-141 B4010 1 PIECE P/N D350-748-141 B4010 1 PIECE P/N D350-748-141 B4042 1 PIECE P/N D350-748-141 B4009 1 PIECE P/N D350-748-241 B4011 1 PIECE P/N D350-748-241 B4011 1 PIECE P/N D350-748-241 B4041 1 PIECE P/N D350-748-241 B4011 4 PIECES P/N D350-748-141 B0023</p>					
<p>100% HARDNESS TESTED 12 PCS 42/43 HRC</p> <p>V.A.I.O. TH. 25 Q.C.</p> <p>08/09/30</p>					

I hereby certify that the material covered by this release note has been inspected and tested and conforms to all specifications relevant thereto in accordance with the conditions of the contract / or purchase order.

ON BEHALF OF VAC AERO INTERNATIONAL INC.

Anna Robinson
Authorized Q.C. Inspector



VACUUM BRAZING - HEAT TREATING - SPECIAL PROCESSING - FURNACE EQUIPMENT
TURBINE COMPONENT OVERHAUL - PLASMA AND OTHER COATINGS



HEAT
TREATING
